

# Project Status Report



## Task Orders

Heart of the Valley Metropolitan Sewerage District (HOVMSD)  
Donohue Project Number 13649

Period | Oct 23 – Nov 19, 2022

Invoice 30

### Activities This Period

- Attended monthly construction progress meeting for November.
- Closed Clean Water Fund Loan and Issued Pay Applications 3.
- Reviewed Contractor submittals and answered Contractor questions.
- Prepared requests for proposals and work change directives.
- Began preparing RFP 006 for the Hauled-In Waste Tank rehabilitation.
- Provided on-site construction observation services.
- Approved Contractor to proceed with RFP 01, 02, and 05.

### Near-Term Activities

- Review contractor submittals and answer contractor questions.
- Prepare work change directives and responses to contractor claims.
- Review monthly pay application.
- Review pricing for RFP 03 and 04. Finalize RFP 006 and send to Contractor for pricing.
- Continue on-site construction observation services.

### Outstanding Issues

- Continue organizing effort to manage contaminated soil found on-site in coordination with WDNR.

### Construction Remarks

- R-Industries continuing the work on the demolition of existing equipment, electrical and piping in progress in Structure 60 (Solids Handling and Filtration Building)
- Removal of concrete is in progress in Str 60 in the old sand filters, once floors are cut additional filter media removed that migrated below filter floor.
- Removal of the old SE (Secondary Effluent) Pumps, Sand Filter Backwash Pumps, Blowers, and associated Electrical Controls has been completed.
- Removal of asphalt, curb, concrete, sidewalk, necessary underground piping, including 42-in SE and FE piping and electrical is complete to begin the work for new Structures 122 and 123.
- Any contaminated soil near Str 123 that has been removed and transported to the Ridgeview RDF Landfill in Whitelaw, WI.
- Ostrenga has completed the excavation and foundation base for new Structure 123 (Filter Splitter Box) and has completed the excavation for the CCT Transfer Box located just to the east.
- Sargent Electric working on demolition and rerouting of conduit and electrical.
- Opening for the new CCT Transfer box is being worked on east of the new Filter Splitter box.
- August Winters completed the rerouting underground piping and utilities around the future Structure 122 (Filter Chemical Storage) on the northside of Structure 60.
- The excavation and grouted micropiles have been completed for Structure 122.
- The start of formwork and rebar work for the foundation grade beams of Str 122 has begun.
- Wisconsin Rebar and CD Smith completed the rebar and formwork for the base slab of Structure 123. CD Smith completed the first concrete pour of the project on the base slab.

# Project Status Report



## Task Orders

Heart of the Valley Metropolitan Sewerage District (HOVMSD)  
Donohue Project Number 13649

Period | Oct 23 – Nov 19, 2022  
Invoice 30

### Progress Photographs

Anthracite being removed from old filters, prior to concrete demolition in Str 60.



Terra installing first grouted micropile for new Str 122 Filter Chemical Storage



# Project Status Report



## Task Orders

Heart of the Valley Metropolitan Sewerage District (HOVMSD)  
Donohue Project Number 13649

Period | Oct 23 – Nov 19, 2022  
Invoice 30

Old Secondary Effluent Pumps removed and wall sleeves capped



Foundation base ready for rebar and concrete for Str 123 Filter Splitter Box



# Project Status Report



## Task Orders

Heart of the Valley Metropolitan Sewerage District (HOVMSD)  
Donohue Project Number 13649

Period | Oct 23 – Nov 19, 2022

Invoice 30

Formwork and rebar ready for Str 123 Filter Splitter Box base slab



Grouted micropiles complete for Str 122 Filter Chemical Storage grade beams, CD Smith starting formwork



# Project Status Report




## Task Orders

Heart of the Valley Metropolitan Sewerage District (HOVMSD)  
Donohue Project Number 13649

Period | Oct 23 – Nov 19, 2022

Invoice 30

Concrete demo work in old filters in Str 60

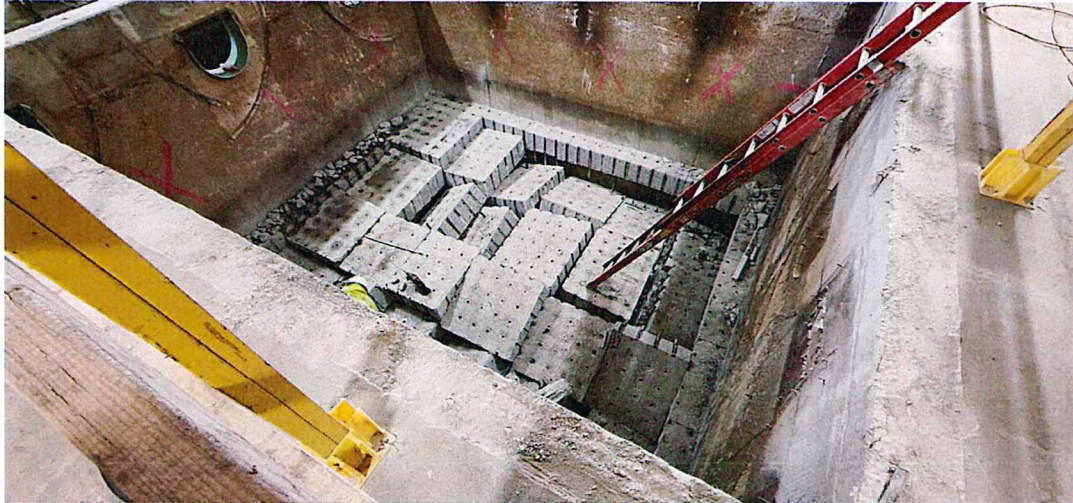

Excavation completed and demo work started for new CCT Transfer Box



# Project Status Report



## Task Orders

Heart of the Valley Metropolitan Sewerage District (HOVMSD)  
Donohue Project Number 13649

Period | Oct 23 – Nov 19, 2022  
Invoice 30

Blankets placed on formwork and rebar for Str 123 Filter Splitter Box, in preparation for first concrete pour



Base slab poured for new Str 123 Filter Splitter Box, first pour of the project

